



CENTER CITY CONNECTOR STREETCAR

Thank you for your interest in the Center City Connector Streetcar. In this weekly update, you'll find information about ongoing construction for the 1st phase of utility work in Pioneer Square.

Project Update:

Night work at 1st Ave and Yesler Way intersection previously scheduled for Monday, November 12 has been rescheduled for tonight

TUESDAY, NOVEMBER 13, AT 9 PM THROUGH WEDNESDAY, NOVEMBER 14, AT 9 AM

Crews will be repairing a drainage line at the 1st Ave and Yesler Way intersection from 9 PM Tuesday, November 13, to 9 AM Wednesday, November 14. The work requires access through the sewer and is scheduled to occur overnight to take advantage of lower sewage flows during that time. This work is weather dependent and will require the intermittent use of a compressor, which may create noise during work hours.

Utility construction in Pioneer Square: What to expect the week of November 11

Crews expect to complete paving and open 1st Ave to traffic and parking by the end of the day today. They'll continue to remove supplies and equipment as work wraps up. While we have a few weeks of work remaining, the majority of 2018 construction is complete, and crews will continue consolidating their footprint in Pioneer Square.

1ST AVE S FROM S JACKSON ST TO S COLUMBIA ST

- Crews will be installing lane striping and roadway markings
- Crews will be landscaping, resetting pavers, and repairing the sidewalk and curb in various locations. This work may require temporary lane closures and detours for people walking and biking.
- Crews will continue consolidating and removing equipment and materials


- Some of the work is weather dependent
- Expect noise, as well as typical construction impacts such as temporary lane closures, increased truck activity, and exhaust

ONGOING TRAFFIC LANE RESTRICTIONS, STREET CLOSURES, AND OTHER IMPACTS

- Temporary lane closures on 1st Ave and 1st Ave S between Cherry St and S Jackson St will occur intermittently until construction is complete
- Intermittent lane closures on S Jackson St and Cherry St for punch list activities
- Construction staging will remain on the south side of James St, between Yesler Way and 2nd Ave
- Typical construction hours are 7 AM – 5 PM, Monday – Friday. Construction-related noise may be heard as early as 6:30 AM as crews refuel equipment and begin staging for the day.
- Expect occasional weekend work
- Expect typical construction impacts such as increased dust, noise, vibration, and truck activity

NOVEMBER 2018 CONSTRUCTION MAP

Subject to change

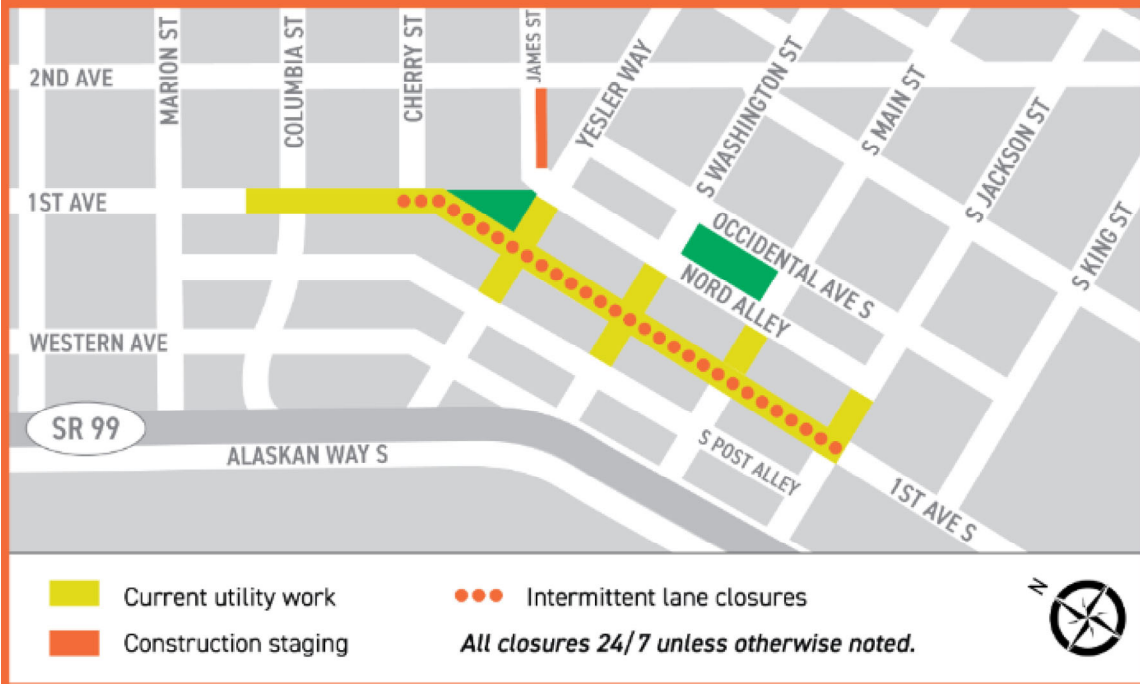

Other nearby work

AREAWAY REPAIR ON THE NORTH SIDE OF COLUMBIA ST BETWEEN 1ST AND POST AVENUES

Areaway repair work began in August and is anticipated to be complete prior to Thanksgiving. This work consists of filling the areaway under the sidewalk with lightweight concrete fill, reconstructing the sidewalk above, and improving entryways to businesses on Columbia St.

For more info or questions about construction, contact us at centercitystreetcar@seattle.gov or our 24/7 hotline, (206) 400-7578. For more information about the project, please visit our [website](#).

To forward this update to others who may be interested in the project, please [click here](#).

Thank you!

Center City Connector Streetcar project team



Seattle
Department of
Transportation

